



CARES Implementation Phase

Rollout #4 PTAX Bi-Weekly Touch Point


February 26, 2025

DAVE YOST

Agenda

- Schedule Review
- Workflows Progress
- ETL Design and Testing Timeline
- End-to-End Testing
- Resources Check-In
- Comments/Questions

Schedule Review

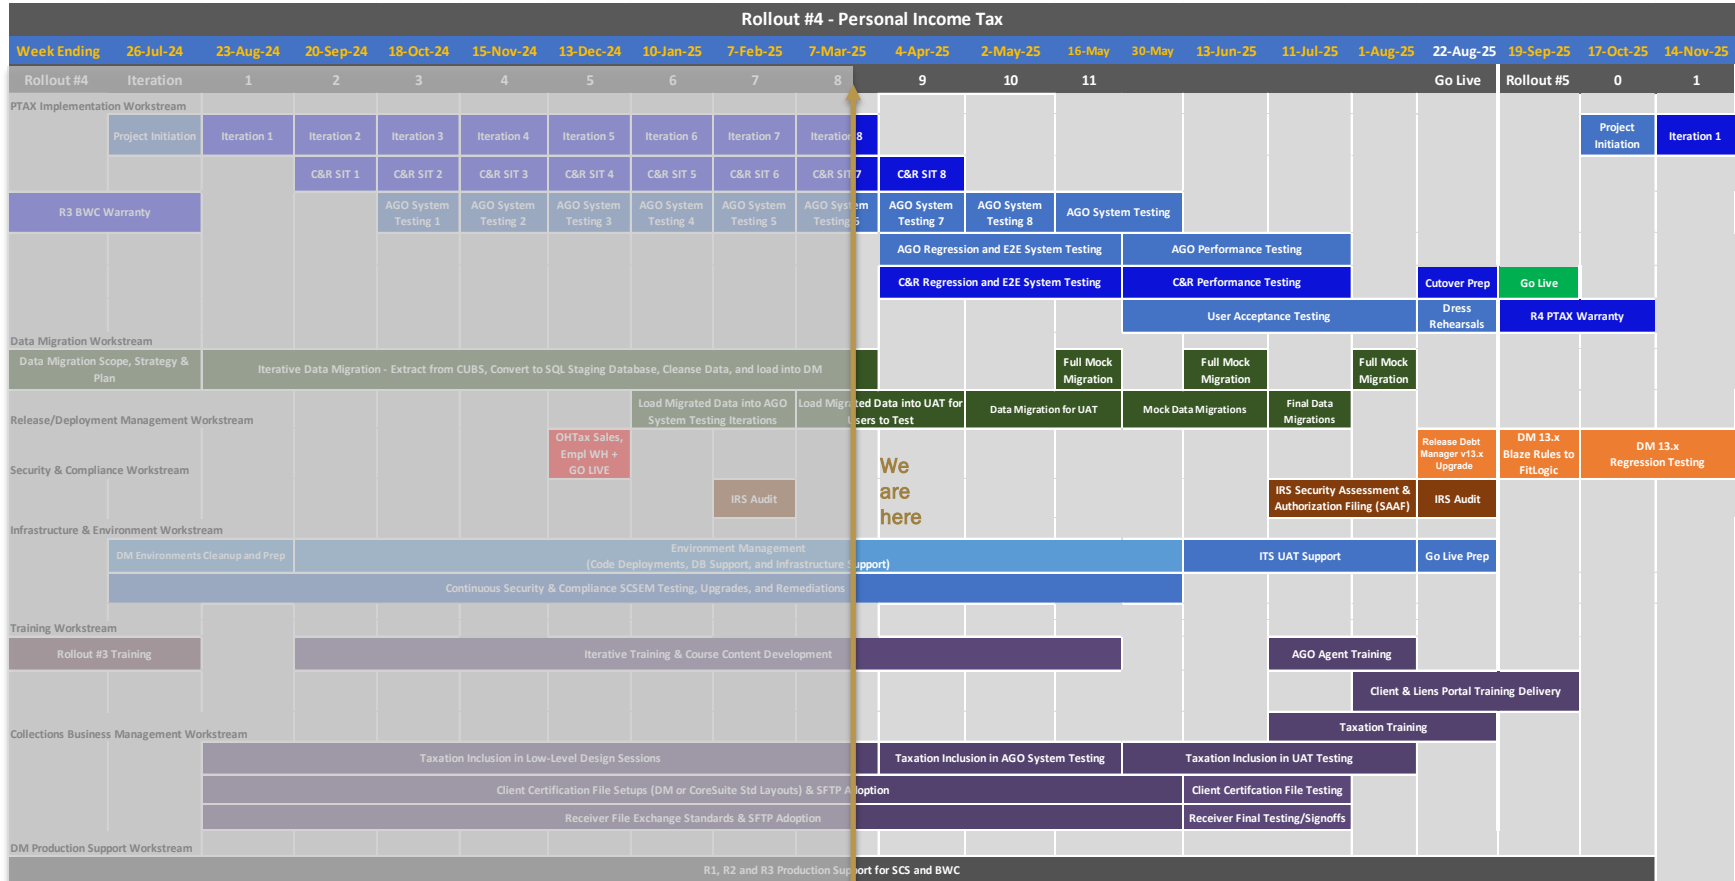

Non-Technical Workflows

Design Session	AGO Owner	Dates Held	Comments
WF-19 Innocent Spouse	Kevin Whitacre, Nicole Brock	8/5/2024-8/13/2024	QA Testing completed; Awaiting End-to-End Testing
WF-48 Tax Collections	Sharnee Jennings, Nick Yono	7/29/2024-8/23/2024	AGO QA Testing in progress
Skip Trace	Shannon Ray, Lucas Ward	6/26/2024-8/12/2024	QA Testing completed; Awaiting End-to-End Testing
Workflow Look-backs	Sharnee Jennings, Nick Yono	8/26/2024-9/27/2024	Wave 1 deployed for AGO QA testing
AC-14 TOPS/OTOP	AGO Accounting/Pat Brobeck/Sharnee Jennings, Nick Yono	9/30/2024-10/1/2024	QA Testing completed; Awaiting End-to-End Testing
WF-33 Offer in Compromise	Kevin Whitacre/Nicole Brock	10/21/2024-11/14/2024	Formal Approval Stage
WF-55 Tax FTP Process	Sharnee Jennings, Nick Yono	11/19/2024	Formal Approval Stage
WF-50 Tax Penalty Abatements	Sharnee Jennings, Nick Yono	12/5/2024-12/13/2024	Formal Approval Stage

Non-Technical Workflows

Design Session	AGO Owner	Dates Held	Comments
OIC Custom View	Nicole Brock; Kevin Whitacre	12/5/2024-12/17/2024	Final Walk-Through completed
WF-49 Tax Memos	Sharnee Jennings/Nick Yono	1/7/2025	In testing with C&R
Unclaimed Funds	Pat Brobeck	2/18/2025 – Present	Design in progress

Technical Workflows

Design Session	AGO Owner	Dates Held	Comments
SOVOS-1099	David Boals, James Seeto	8/1/2024-8/20/2024	QA Testing completed; Awaiting End-to-End Testing
Skip Tracing Interface	Shannon Ray, Lucas Ward	6/26/2024-8/21/2024	QA Testing completed; Awaiting End-to-End Testing
BKY Skip Tracing	Shannon Ray, Lucas Ward, Trish Lazich	8/5/2024-8/12/2024	QA Testing completed; Awaiting End-to-End Testing
Migration Discussions	Billy Miller, Timothy Greene	7/29/2024-Present	Ongoing Migration discussions taking place; sixth iterative load has been completed and results are currently under review.
Certification (9020) Interface	Sharnee Jennings, Nick Yono	8/26/2024-8/29/2024	AGO QA Testing in progress
Address update 9008	Sharnee Jennings, Nick Yono	8/29/2024-9/5/2024	QA Testing completed; Awaiting End-to-End Testing
Non-Financial 9011.40	Sharnee Jennings, Nick Yono	9/3/2024-9/5/2024	QA Testing completed; Awaiting End-to-End Testing
Decert 9407.40	Sharnee Jennings, Nick Yono	9/5/2024 – 9/23/2024	QA Testing completed; Awaiting End-to-End Testing

Technical Workflows - Continued

Design Session	AGO Owner	Dates Held	Comments
Transaction Import 9011	Sharnee Jennings, Nick Yono	9/9/2024 – 9/16/2024	QA Testing completed; Awaiting End-to-End Testing
TOPS/OTOP Interface	Patrick Brobeck, Sharnee Jennings, Nick Yono	9/30/2024-11/12/2024	AGO QA Testing in progress
True Up Webservice	Sharnee Jennings, Nick Yono	9/17/2024 – Present	Formal approval stage Current approach: Tax developer working with C&R developer support to adjust OHTax programming to call DM Rest API. Delivery/QA rough estimate – late January 2025.
Transaction Export IB.8050	Sharnee Jennings, Nick Yono	1/10/2025-2/4/2025	Formal Approval Stage
Non-Financial Export IB.8050.40	Sharnee Jennings, Nick Yono	1/10/2025-2/4/2025	Formal Approval Stage
DataExtract 8050.98/99	Sharnee Jennings, Nick Yono	1/17/2025-2/4/2025	Pending deployment from C&R to AGO QA for testing

Technical Workflows - Continued

Design Session	AGO Owner	Dates Held	Comments
Tax Transaction Clean-Up ETL	Sharnee Jennings, Nick Yono	2/6/2025 - Present	Design in progress

Design and Testing for ETLs

ETL Interface Name	Design Sessions		QA Testing		E2E Testing *		UAT	
	Start Date	End Date	Start Date	End Date	Start Date	End Date	Start Date	End Date
Address Update 9008	8/26/2024	9/20/2024	10/21/2024	11/15/2024	3/10/2025	4/4/2025	5/19/2025	8/1/2025
Transaction Import 9011	8/26/2024	9/20/2024	10/21/2024	11/15/2024	3/10/2025	4/4/2025	5/19/2025	8/1/2025
NonFinancial 9011.40	8/26/2024	9/20/2024	10/21/2024	11/15/2024	3/10/2025	4/4/2025	5/19/2025	8/1/2025
Cert 9020	8/26/2024	9/20/2024	10/21/2024	11/15/2024	3/10/2025	4/4/2025	5/19/2025	8/1/2025
Decert 9407.40	8/26/2024	9/20/2024	11/18/2024	12/13/2024	3/10/2025	4/4/2025	5/19/2025	8/1/2025
True Up Web Service	8/26/2024	9/20/2024	TBD**	TBD**	TBD**	TBD**	TBD**	TBD**
Transaction Export (IB.8050)	1/13/2025	2/7/2025	3/10/2025	4/4/2025	4/7/2025	5/5/2025	5/19/2025	8/1/2025
NonFin Export (IB.8050.40)	1/13/2025	2/7/2025	3/10/2025	4/4/2025	4/7/2025	5/5/2025	5/19/2025	8/1/2025
DATAEXTRACT 8050.98	1/17/2025	2/7/2025	4/7/2025	5/2/2025	5/5/2025	5/16/2025	5/19/2025	8/1/2025
DATAEXTRACT 8050.99	Duplicate interface - absorbed into 8050.98							

*Estimated date ranges

** Dependent Upon Tax development timeline

Note: the only environments which are hardened for FTI are PRE01 (UAT), PROD (Production), TST01 (QA/UAT for Production Support), and R&D (for migration purposes)

End-to-End (E2E) Testing

Targeted start date: 3/10/2025 | Targeted end date: 5/19/2025

Items to be tested with Taxation

Inbound (Taxation → AGO)

File Name	Projected E2E Start Date
XCI – Cert 9020	3/10/2025
XNI – NonFinancial 9011.40	3/17/2025
XDI – Decert 9407.40	3/19/2025
XFI – Transaction Import 9011	3/26/2025
XAI – Address Update 9008	4/2/2025

Outbound (AGO → Taxation)

File Name	Projected E2E Start Date
XFO – Transaction Export (IB.8050)	4/4/2025
XNFO – NonFin Export (IB.8050.40)	4/7/2025
XADO – Tax Archive DataExtract (8050.98)	4/7/2025
File Name	Projected E2E Start Date
True Up Web Service (Real-Time API call)	TBD

Resources Check-In

Comments/Questions

Thank You!

